


ID	Task Name	Duration	Act. Start	Act. Finish	% Comp.	Act. Dur.	Rem. Dur.	October 2024	November 2024	December 2024	January 2025	February 2025	March 2025	April 2025	May 2025	June 2025	July 2025	August 2025	September 2025	October 2025						
1	Wilmington Ave Safe Streets	254 days	Tue 10/1/24	NA	67%	168.96 days	85.04 days	67%																		
2	Project Milestones	254 days	Tue 10/1/24	NA	0%	0 days	254 days	0%																		
3	Notice of Award	0 days	Tue 10/1/24	Tue 10/1/24	100%	0 days	0 days																			
4	Contract Award	0 days	Wed 10/9/24	Wed 10/9/24	100%	0 days	0 days																			
5	Fully Executed Contract (Pending)	0 days	Fri 11/1/24	Fri 11/1/24	100%	0 days	0 days																			
6	Preconstruction Meeting	0 days	Thu 11/7/24	Thu 11/7/24	100%	0 days	0 days																			
7	Notice to Proceed	0 days	Mon 12/9/24	Mon 12/9/24	100%	0 days	0 days																			
8	Substantial Completion	0 days	NA	NA	0%	0 days	0 days																			
9	Final Completion	0 days	NA	NA	0%	0 days	0 days																			
10	Submittals - Long Lead Items	62 days	Fri 11/1/24	Thu 1/30/25	100%	62 days	0 days																			
11	Prepare & Submit	59 days	Fri 11/1/24	Mon 1/27/25	100%	59 days	0 days																			
12	Site Amenities	59 days	Fri 11/1/24	Mon 1/27/25	100%	59 days	0 days																			
13	Bus Shelter	7 days	Thu 1/16/25	Mon 1/27/25	100%	7 days	0 days																			
14	Bench	19 days	Fri 11/1/24	Wed 11/27/24	100%	19 days	0 days																			
15	Trash Receptacle	19 days	Fri 11/1/24	Wed 11/27/24	100%	19 days	0 days																			
16	Traffic Signal	8 days	Fri 11/1/24	Tue 11/12/24	100%	8 days	0 days																			
17	Push Button Posts	8 days	Fri 11/1/24	Tue 11/12/24	100%	8 days	0 days																			
18	Signals	8 days	Fri 11/1/24	Tue 11/12/24	100%	8 days	0 days																			
19	APS Push Buttons	5 days	Fri 11/1/24	Thu 11/7/24	100%	5 days	0 days																			
20	Video Detection Cameras	4 days	Fri 11/1/24	Wed 11/6/24	100%	4 days	0 days																			
21	Street Name Signs	8 days	Fri 11/1/24	Tue 11/12/24	100%	8 days	0 days																			
22	Street Lighting	4 days	Fri 11/1/24	Wed 11/6/24	100%	4 days	0 days																			
23	Lithonia Aluminum Poles	4 days	Fri 11/1/24	Wed 11/6/24	100%	4 days	0 days																			
24	Lithonia Luminaires	4 days	Fri 11/1/24	Wed 11/6/24	100%	4 days	0 days																			
25	Review & Approve	59 days	Wed 11/6/24	Thu 1/30/25	100%	59 days	0 days																			
26	Site Amenities	43 days	Thu 11/28/24	Thu 1/30/25	100%	43 days	0 days																			
27	Bus Shelter	4 days	Mon 1/27/25	Thu 1/30/25	100%	4 days	0 days																			
28	Bench	10 days	Thu 11/28/24	Wed 12/11/24	100%	10 days	0 days																			
29	Trash Receptacle	10 days	Thu 11/28/24	Wed 12/11/24	100%	10 days	0 days																			
30	Traffic Signal	7 days	Wed 11/6/24	Thu 11/14/24	100%	7 days	0 days																			
31	Push Button Posts	3 days	Tue 11/12/24	Thu 11/14/24	100%	3 days	0 days																			
32	Signals	3 days	Tue 11/12/24	Thu 11/14/24	100%	3 days	0 days																			
33	APS Push Buttons	5 days	Fri 11/8/24	Thu 11/14/24	100%	5 days	0 days																			
34	Video Detection Cameras	6 days	Wed 11/6/24	Wed 11/13/24	100%	6 days	0 days																			
35	RSNS	2 days	Tue 11/12/24	Wed 11/13/24	100%	2 days	0 days																			
36	Street Lighting	5 days	Wed 11/6/24	Tue 11/12/24	100%	5 days	0 days																			
37	Lithonia Aluminum Poles	5 days	Wed 11/6/24	Tue 11/12/24	100%	5 days	0 days																			
38	Lithonia Luminaires	5 days	Wed 11/6/24	Tue 11/12/24	100%	5 days	0 days																			
39	Long Lead Items	144 days	Wed 11/13/24	NA	78%	111.97 days	32.03 days	78%																		
40	Site Amenities	123 days	Thu 12/12/24	NA	55%	68.01 days	54.99 days	55%																		
41	Bus Shelter	90 days	Fri 1/31/25	NA	16%	14 days	76 days	16%																		
42	Bench	40 days	Thu 12/12/24	Wed 2/19/25	100%	40 days	0 days																			
43	Trash Receptacle	40 days	Thu 12/12/24	Wed 2/19/25	100%	40 days	0 days																			
44	Traffic Signal	101 days	Thu 11/14/24	NA	86%	86.76 days	14.24 days	86%																		
45	Push Button Posts	100 days	Fri 11/15/24	NA	66%	66 days	34 days	66%																		
46	Signals	75 days	Fri 11/15/24	NA	88%	66 days	9 days	88%																		
47	APS Push Buttons	60 days	Fri 11/15/24	Thu 2/20/25	100%	60 days	0 days																			
48	Video Detection Cameras	60 days	Thu 11/14/24	Wed 2/19/25	100%	60 days	0 days																			
49	RSNS	10 days	Thu 11/14/24	Wed 11/27/24	100%	10 days	0 days																			
50	Street Lighting	30 days	Wed 11/13/24	Tue 12/24/24	100%	30 days	0 days																			
51	Lithonia Aluminum Poles	30 days	Wed 11/13/24	Tue 12/24/24	100%	30 days	0 days																			
52	Lithonia Luminaires	30 days	Wed 11/13/24	Tue 12/24/24	100%	30 days	0 days																			
53	Preconstruction Activities	26 days	Fri 11/1/24	Fri 12/6/24	100%	26 days	0 days																			
54	Establish Laydown Yard	26 days	Fri 11/1/24	Fri 12/6/24	100%	26 days	0 days																			
55	Layout & USA	5 days	Mon 11/25/24	Fri 11/29/24	100%	5 days	0 days																			
56	Construction Activities	194 days	Mon 12/9/24	NA	49%	95.31 days	98.69 days	49%																		
57	General	41 days	Mon 12/9/24	Fri 2/14/25	100%	41 days	0 days																			
58	Mobilization	2 days	Mon 12/9/24	Tue 12/10/24	100%	2 days	0 days																			
59	Install BMPs	3 days	Wed 12/11/24	Fri 12/13/24	100%	3 days	0 days																			
60	Survey & Layout	15 days	Mon 12/9/24	Mon 12/30/24	100%	15 days	0 days																			
61	Pothole	8 days	Mon 12/23/24	Fri 1/3/25	100%	8 days	0 days																			
62	Clear & Grub - Remove Existing Trees	0 days	Thu 2/13/25	Fri 2/14/25	100%	0 days	0 days																			
63	Concrete Work (Curb Ramps, Sidewalk, Driveways, Bus Pads, Cross Gutters, Etc.)	114 days	Wed 12/18/24	NA	52%	59.26 days	54.74 days	52%																		
64	Southbound Wilmington	43 days	Wed 12/18/24	Fri 2/28/25	100%	43 days	0 days																			
65	Sawcut	1 day	Wed 12/18/24	Fri 12/27/24	100%	1 day	0 days																			
66	Demo Existing Improvements	21 days	Mon 1/6/25	Tue 2/4/25	100%	21 days	0 days																			
67	Install Crushed Misc. Base	23 days	Wed 1/8/25	Tue 2/11/25	100%	23 days	0 days																			
68	Grade for Concrete Improvements	20 days	Wed 1/8/25	Tue 2/11/25	100%	20 days	0 days																			
69	Pour Concrete Improvements	28 days	Mon 1/13/25	Thu 2/27/25	100%	28 days	0 days																			
70	Construct Slotpatch	4 days	Mon 1/20/25	Fri 2/21/25	100%	4 days	0 days																			
71	Install Handrail	1 day	Fri 2/28/25	Fri 2/28/25	100%	1 day	0 days																			



Legend for Gantt Chart symbols and colors:

- Critical** (Red line)
- Critical Split** (Red dashed line)
- Critical Progress** (Red bar)
- Task** (Blue bar)
- Task Progress** (Blue bar with arrow)
- Split** (Red dashed line)
- Manual Task** (Dotted blue bar)
- Start-only** (Blue bar with arrow)
- Finish-only** (Blue bar with arrow)
- Duration-only** (Blue bar)
- Baseline** (Black bar)
- Baseline Split** (Black dashed bar)
- Baseline Milestone** (Black diamond)
- Milestone** (Black diamond)
- Summary Progress** (Black bar)
- Summary** (Black bar)
- Manual Summary** (Black bar)
- Project Summary** (Black bar)
- External Tasks** (Black bar)
- External Milestone** (Black diamond)
- Inactive Task** (Grey bar)
- Inactive Milestone** (Grey diamond)
- Inactive Summary** (Grey bar)
- Deadline** (Red vertical line)
- Slippage** (Green arrow)

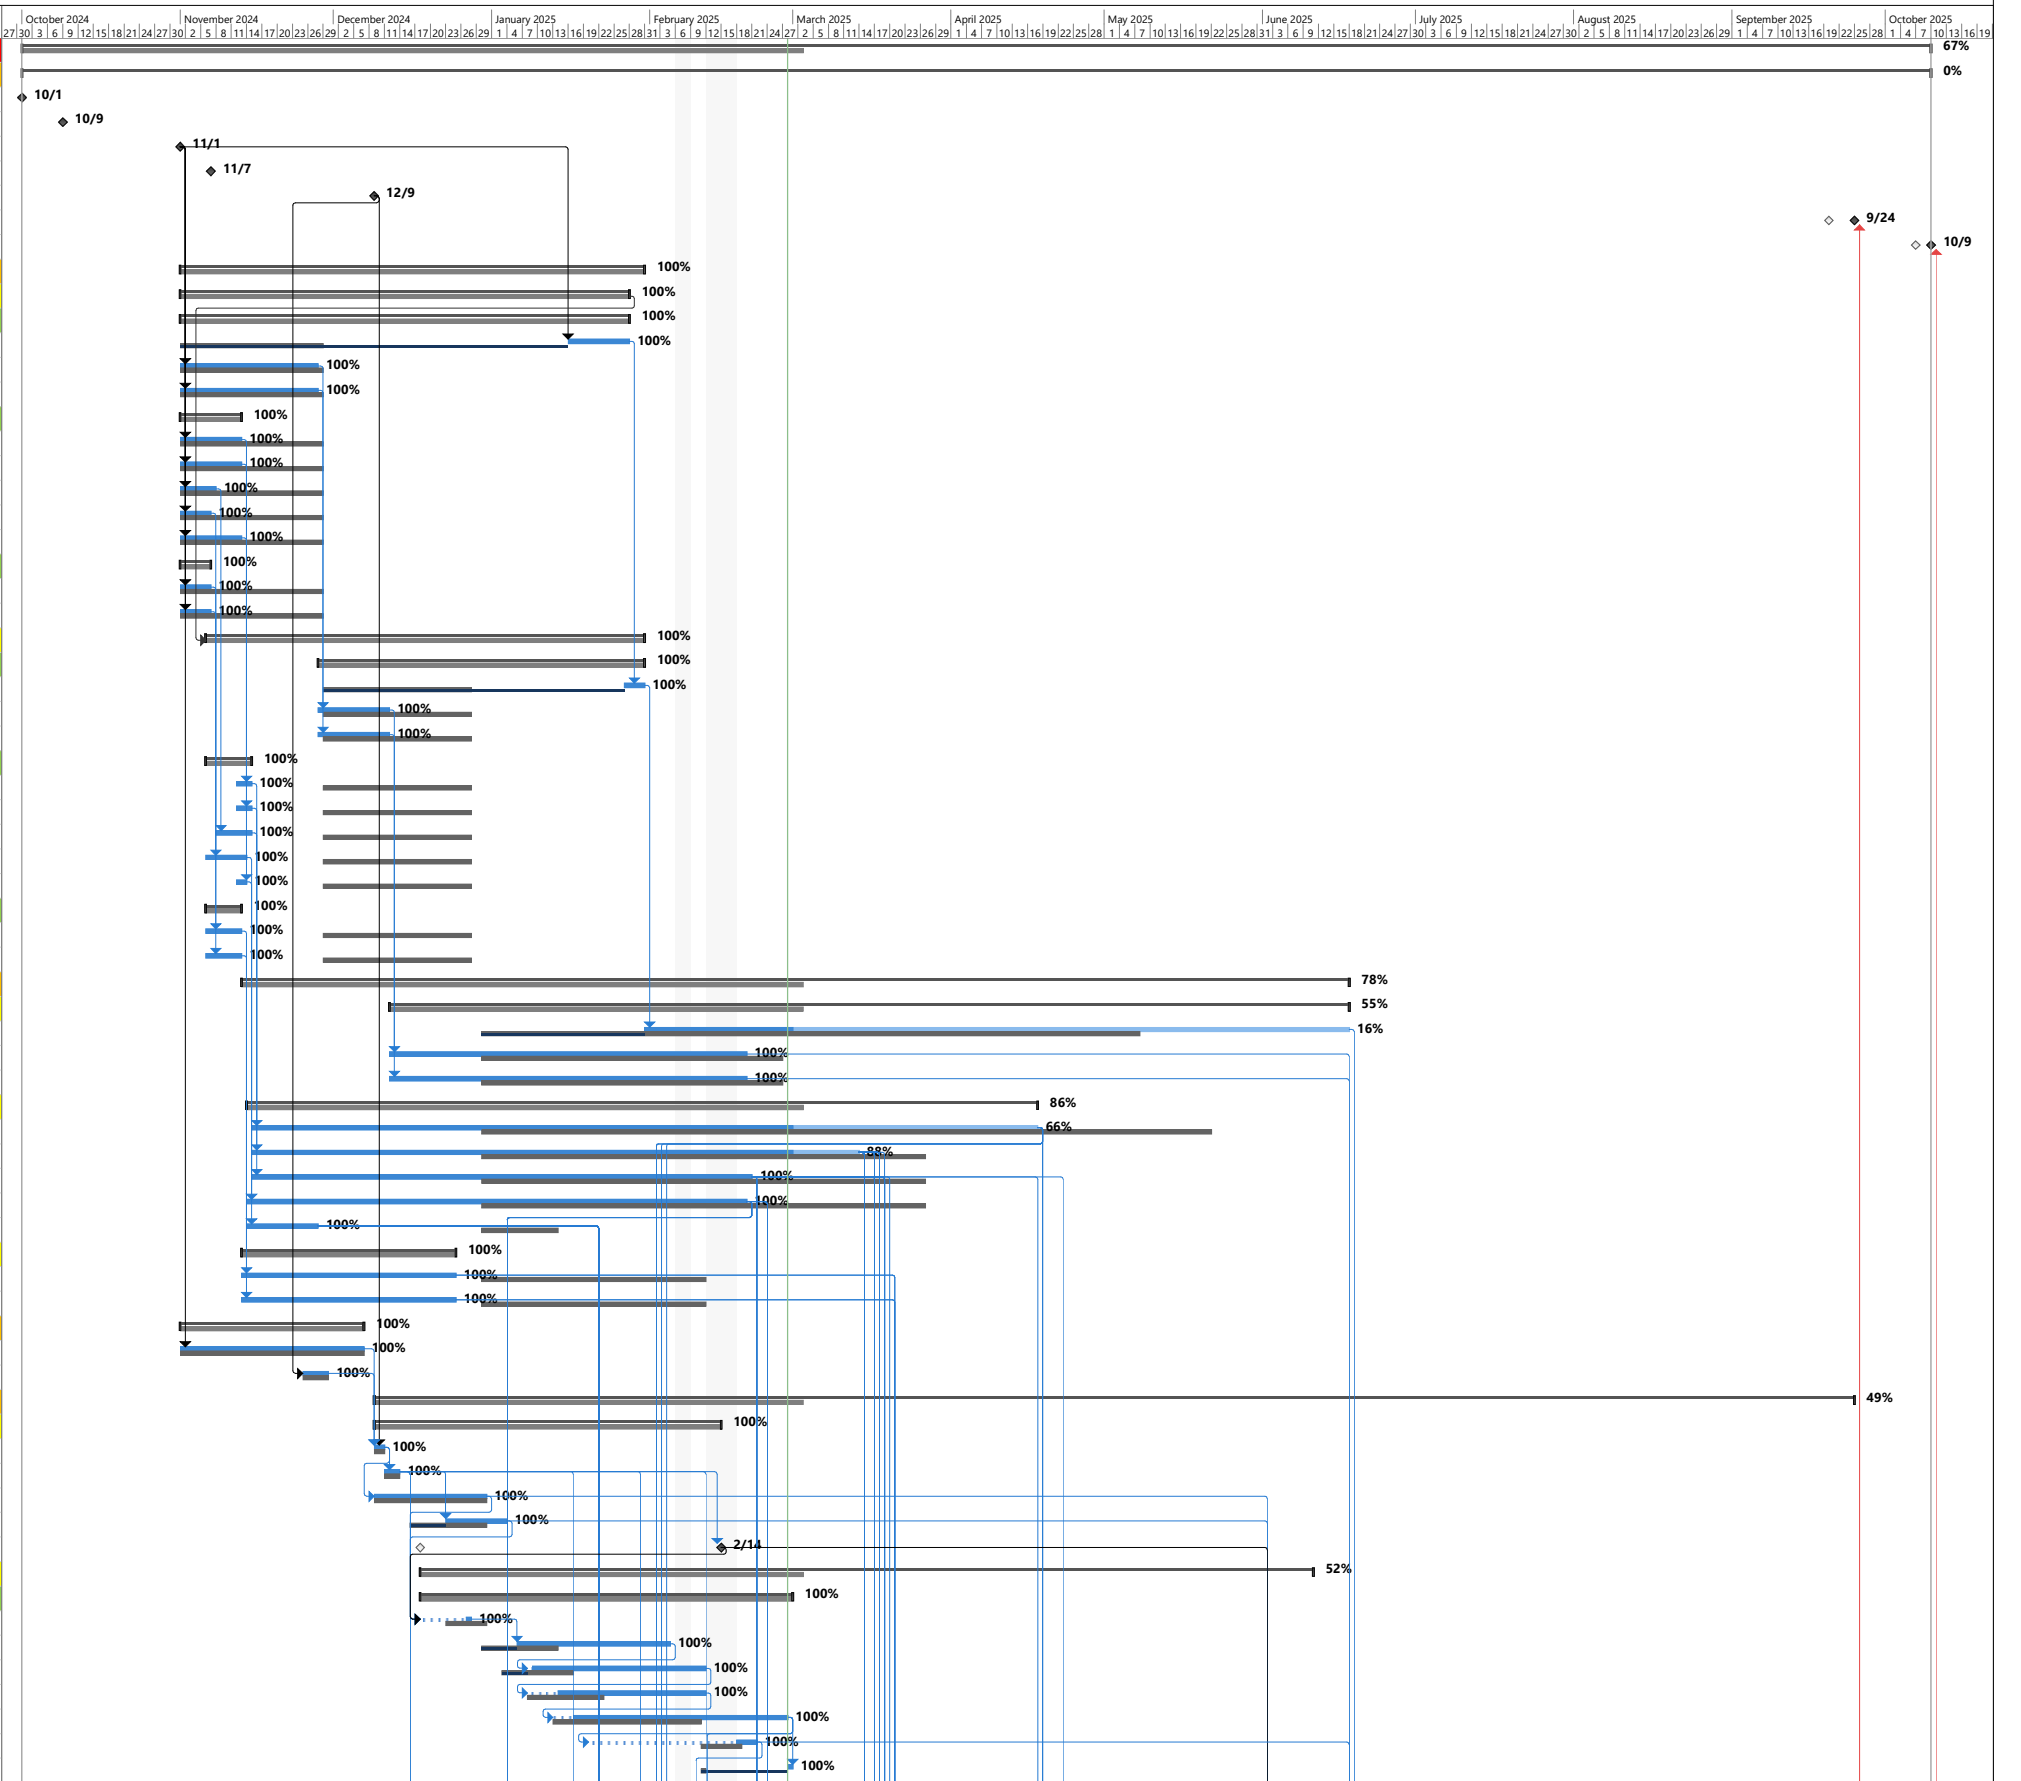
